





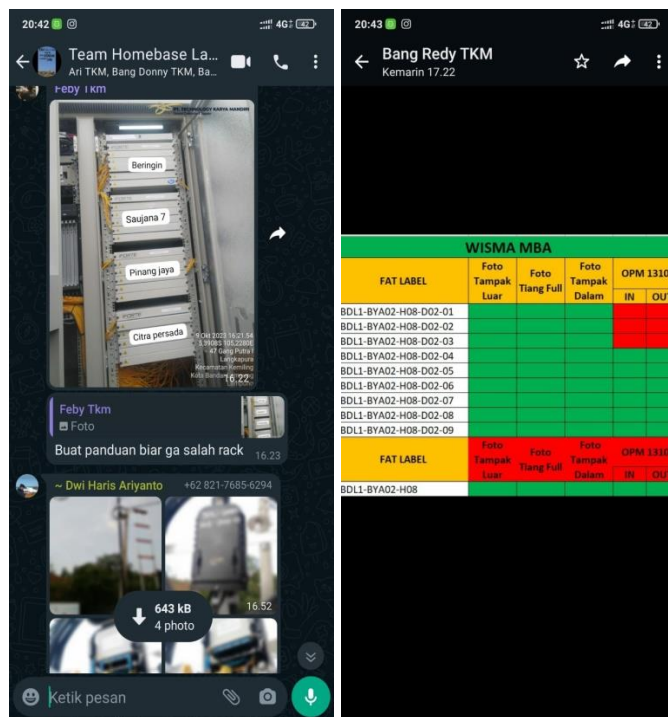

LAMPIRAN

Lampiran 1 Data Pelaporan Melalui Chating

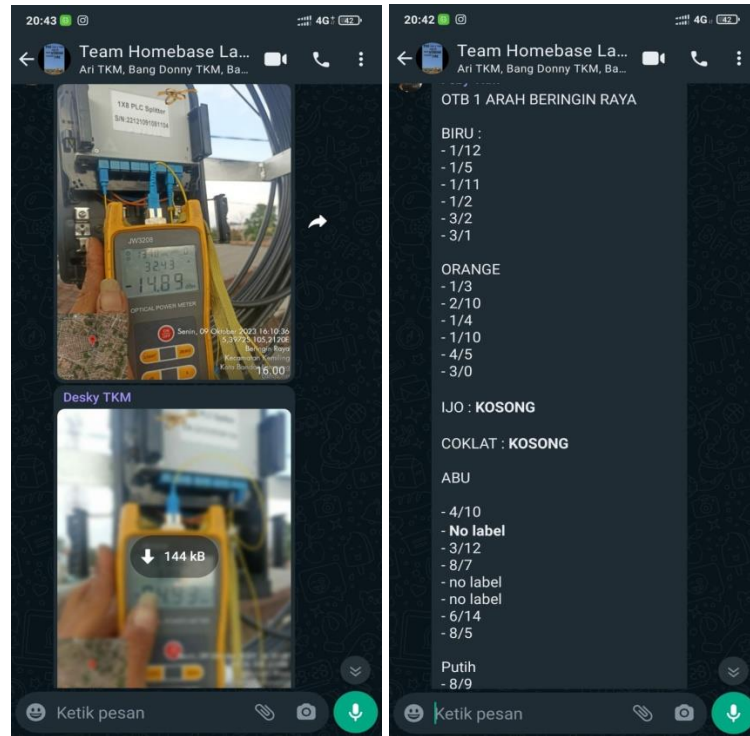

Lampiran 2 Data Rekap Hasil Pelaporan Menggunakan Excel

TARGET BULAN SEPTEMBER PT TECHNOLOGY KARYA MANDIRI													
No	Area	Target HP IFORTE Awal	Komitmen Mitra Re Baseline	ACHIEV WEEK 36	ACHIEV WEEK 37	ACHIEV WEEK 38	ACHIEV WEEK 39	TOTAL HP ACHIEVEMENT versi TKM 4-10-23	TOTAL HP ACHIEVEMENT versi IFORTE 2-10-23	Komitmen HP yg harus di Capai s/d tgl 4 Okt 23 (Iforte)	Selisih HP antara TKM & iforte	BOBOT RFS TKM terhadap Re Baseline %	ket
1	Samarinda	2,000	1,410	374	84	110	423	991	960	450	31	70.28%	Cluster habis/ada BAUT yg belum Approv
2	Pekanbaru	5,500	3,701	308	1,513	561	1,024	3,406	2,717	984	689	92.03%	
3	Lampung	5,000	3,002	299	-	1,604	954	2,857	2,567	435	290	95.17%	
4	Padang	2,000	490	231	-	42	165	438	497	(7)	(59)	89.39%	Aman, nilai HP iforte lebih 7 HP
5	Lombok Barat	1,000	1,006	-	40	120	570	730	726	280	4	72.56%	
6	Lombok Timur	2,500	1,515	-	-	275	1,356	1,631	1,233	282	398	107.66%	
7	Mataram	2,000	1,821	500	395	477	355	1,727	1,697	124	30	94.84%	Cluster habis/ada BAUT yg belum Approv
8	Manado	1,700	1,197	-	730	468	188	1,386	1,150	47	236	115.79%	Aman
9	Pontianak	-	-	-	-	276	-	276	275	(275)	1	100.36%	Aman
Jumlah		8	21,700	14,142	1,712	2,762	3,933	5,035	13,442	11,940	1,502	1,620	
				12.1%	19.5%	27.8%	35.6%	95.1%	84.4%	10.6%			

No	Section Pole ID	Longitude	Latitude	Position (R/L)	Concrete foundation	Pole erection (Verticality)	Accessories				Accessories
							Stank Slack	Dead End	Breket A	Thimble	
1	DD1-NP01	113.921653	-2.21887467	R			2	2	2		
2	DD1-NP02	113.9218581	-2.21886825	R			2	2	2		
3	DD2-NP03	113.9222191	-2.21877658	R			1	2	2		
4	DD2-NP04	113.9222609	-2.21915521	L			1	2	2		
5	DD2-NP05	113.9223367	-2.21954779	R			1	2	2		
6	DD2-NP06	113.9225042	-2.21951192	R			2	2	2		
7	DD2-NP07	113.9228173	-2.21947605	R			1	2	2		
8	DD2-NP08	113.9220635	-2.21962551	L			1	2	2	
